
Balfour Beatty VINCI Working in partnership with HS2


Castle Bromwich Town Council – 27/01/2021

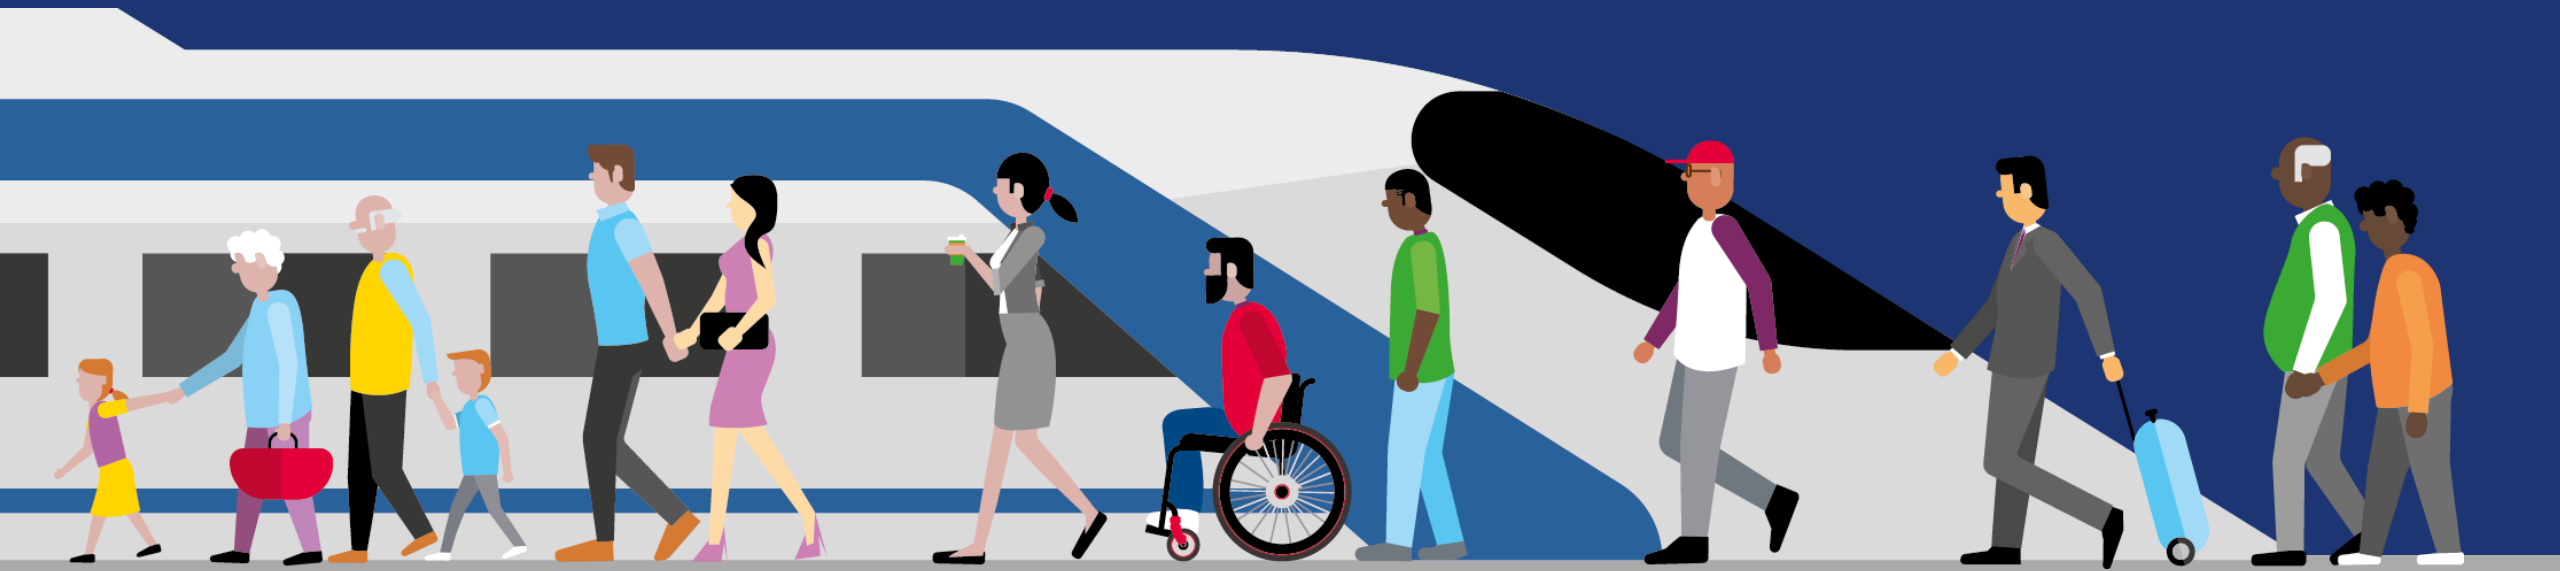


Construction works in your area...

Traffic Routes

- This route is the associated with East portal sites.
- Movements of 40 in and out per day.
- Traffic to come in through Water Orton and leave through Castle Bromwich entering onto main strategic road network.
- HGV movements to increase from Monday 1st February 2021

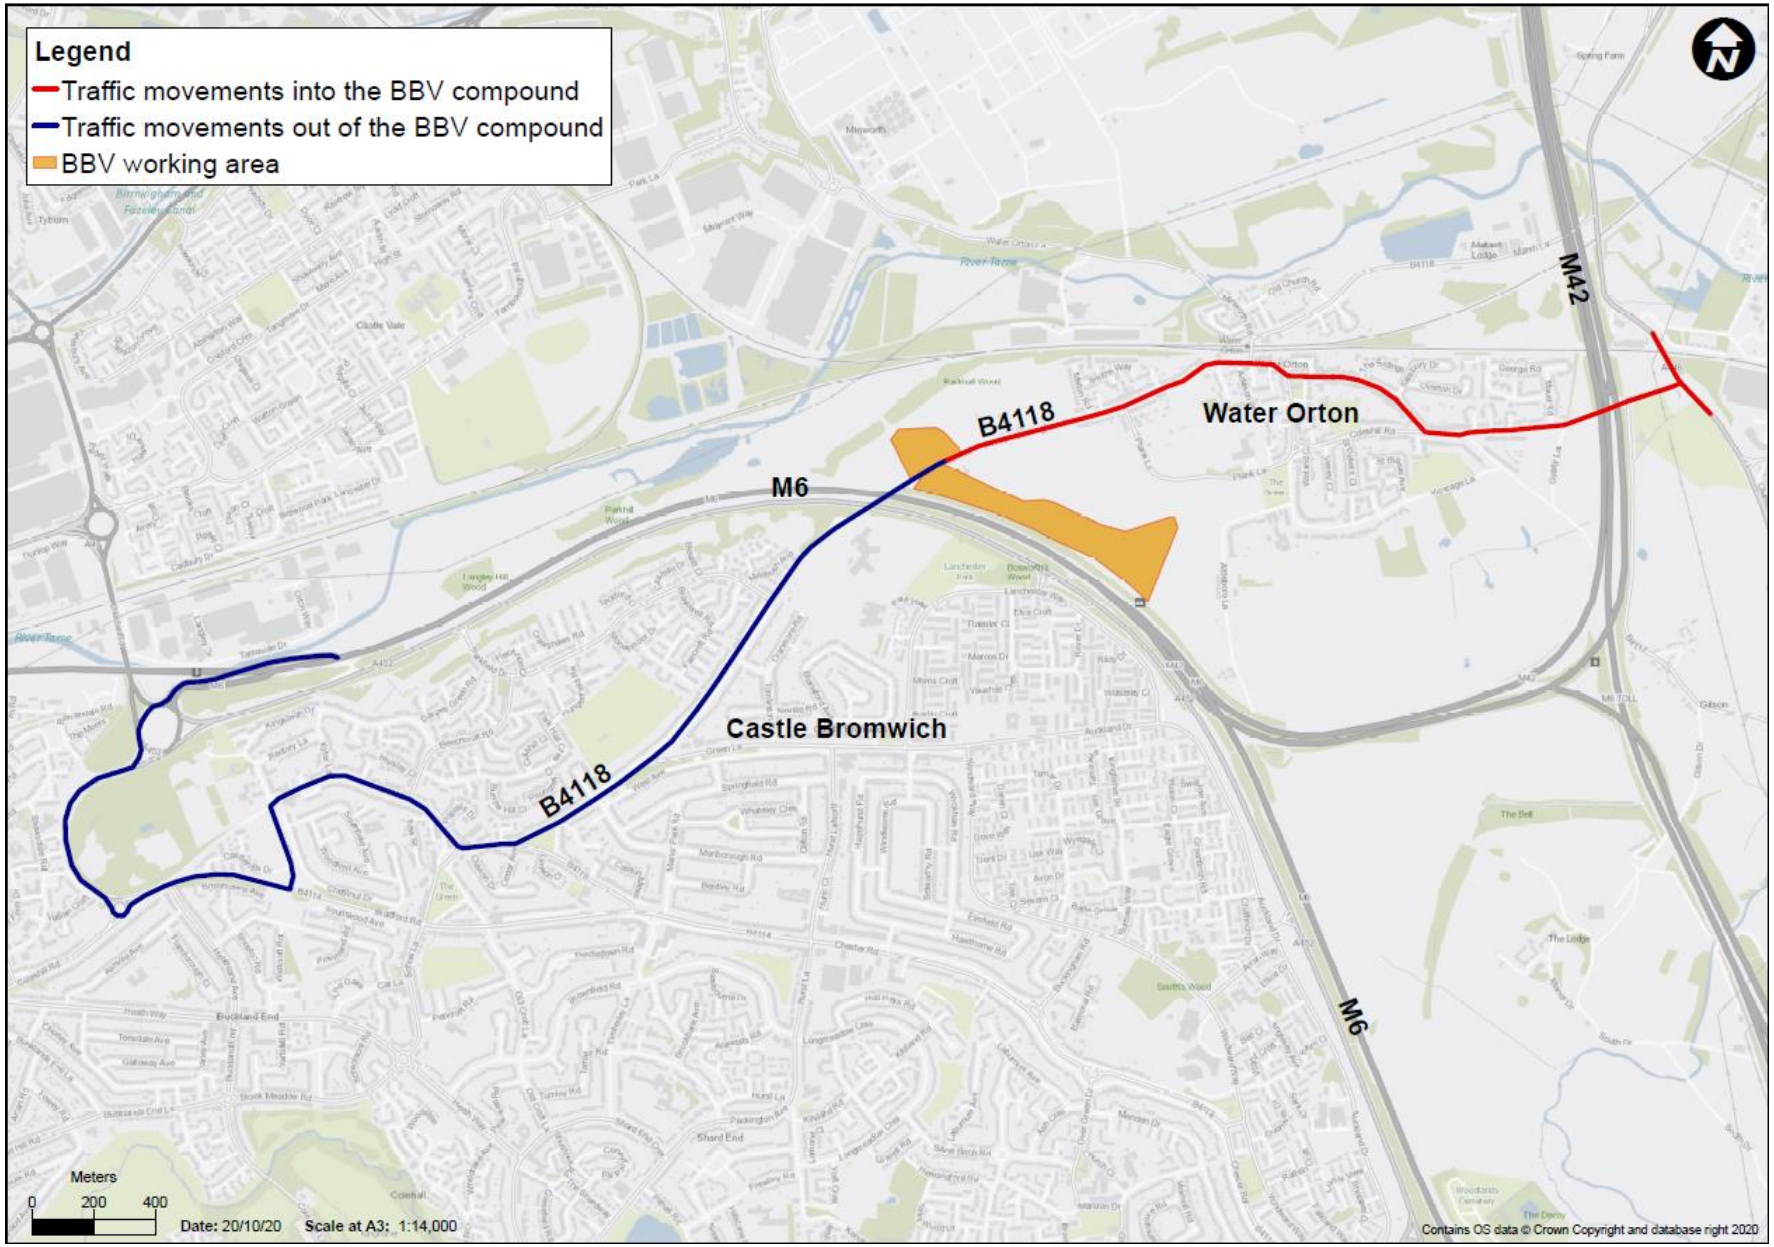

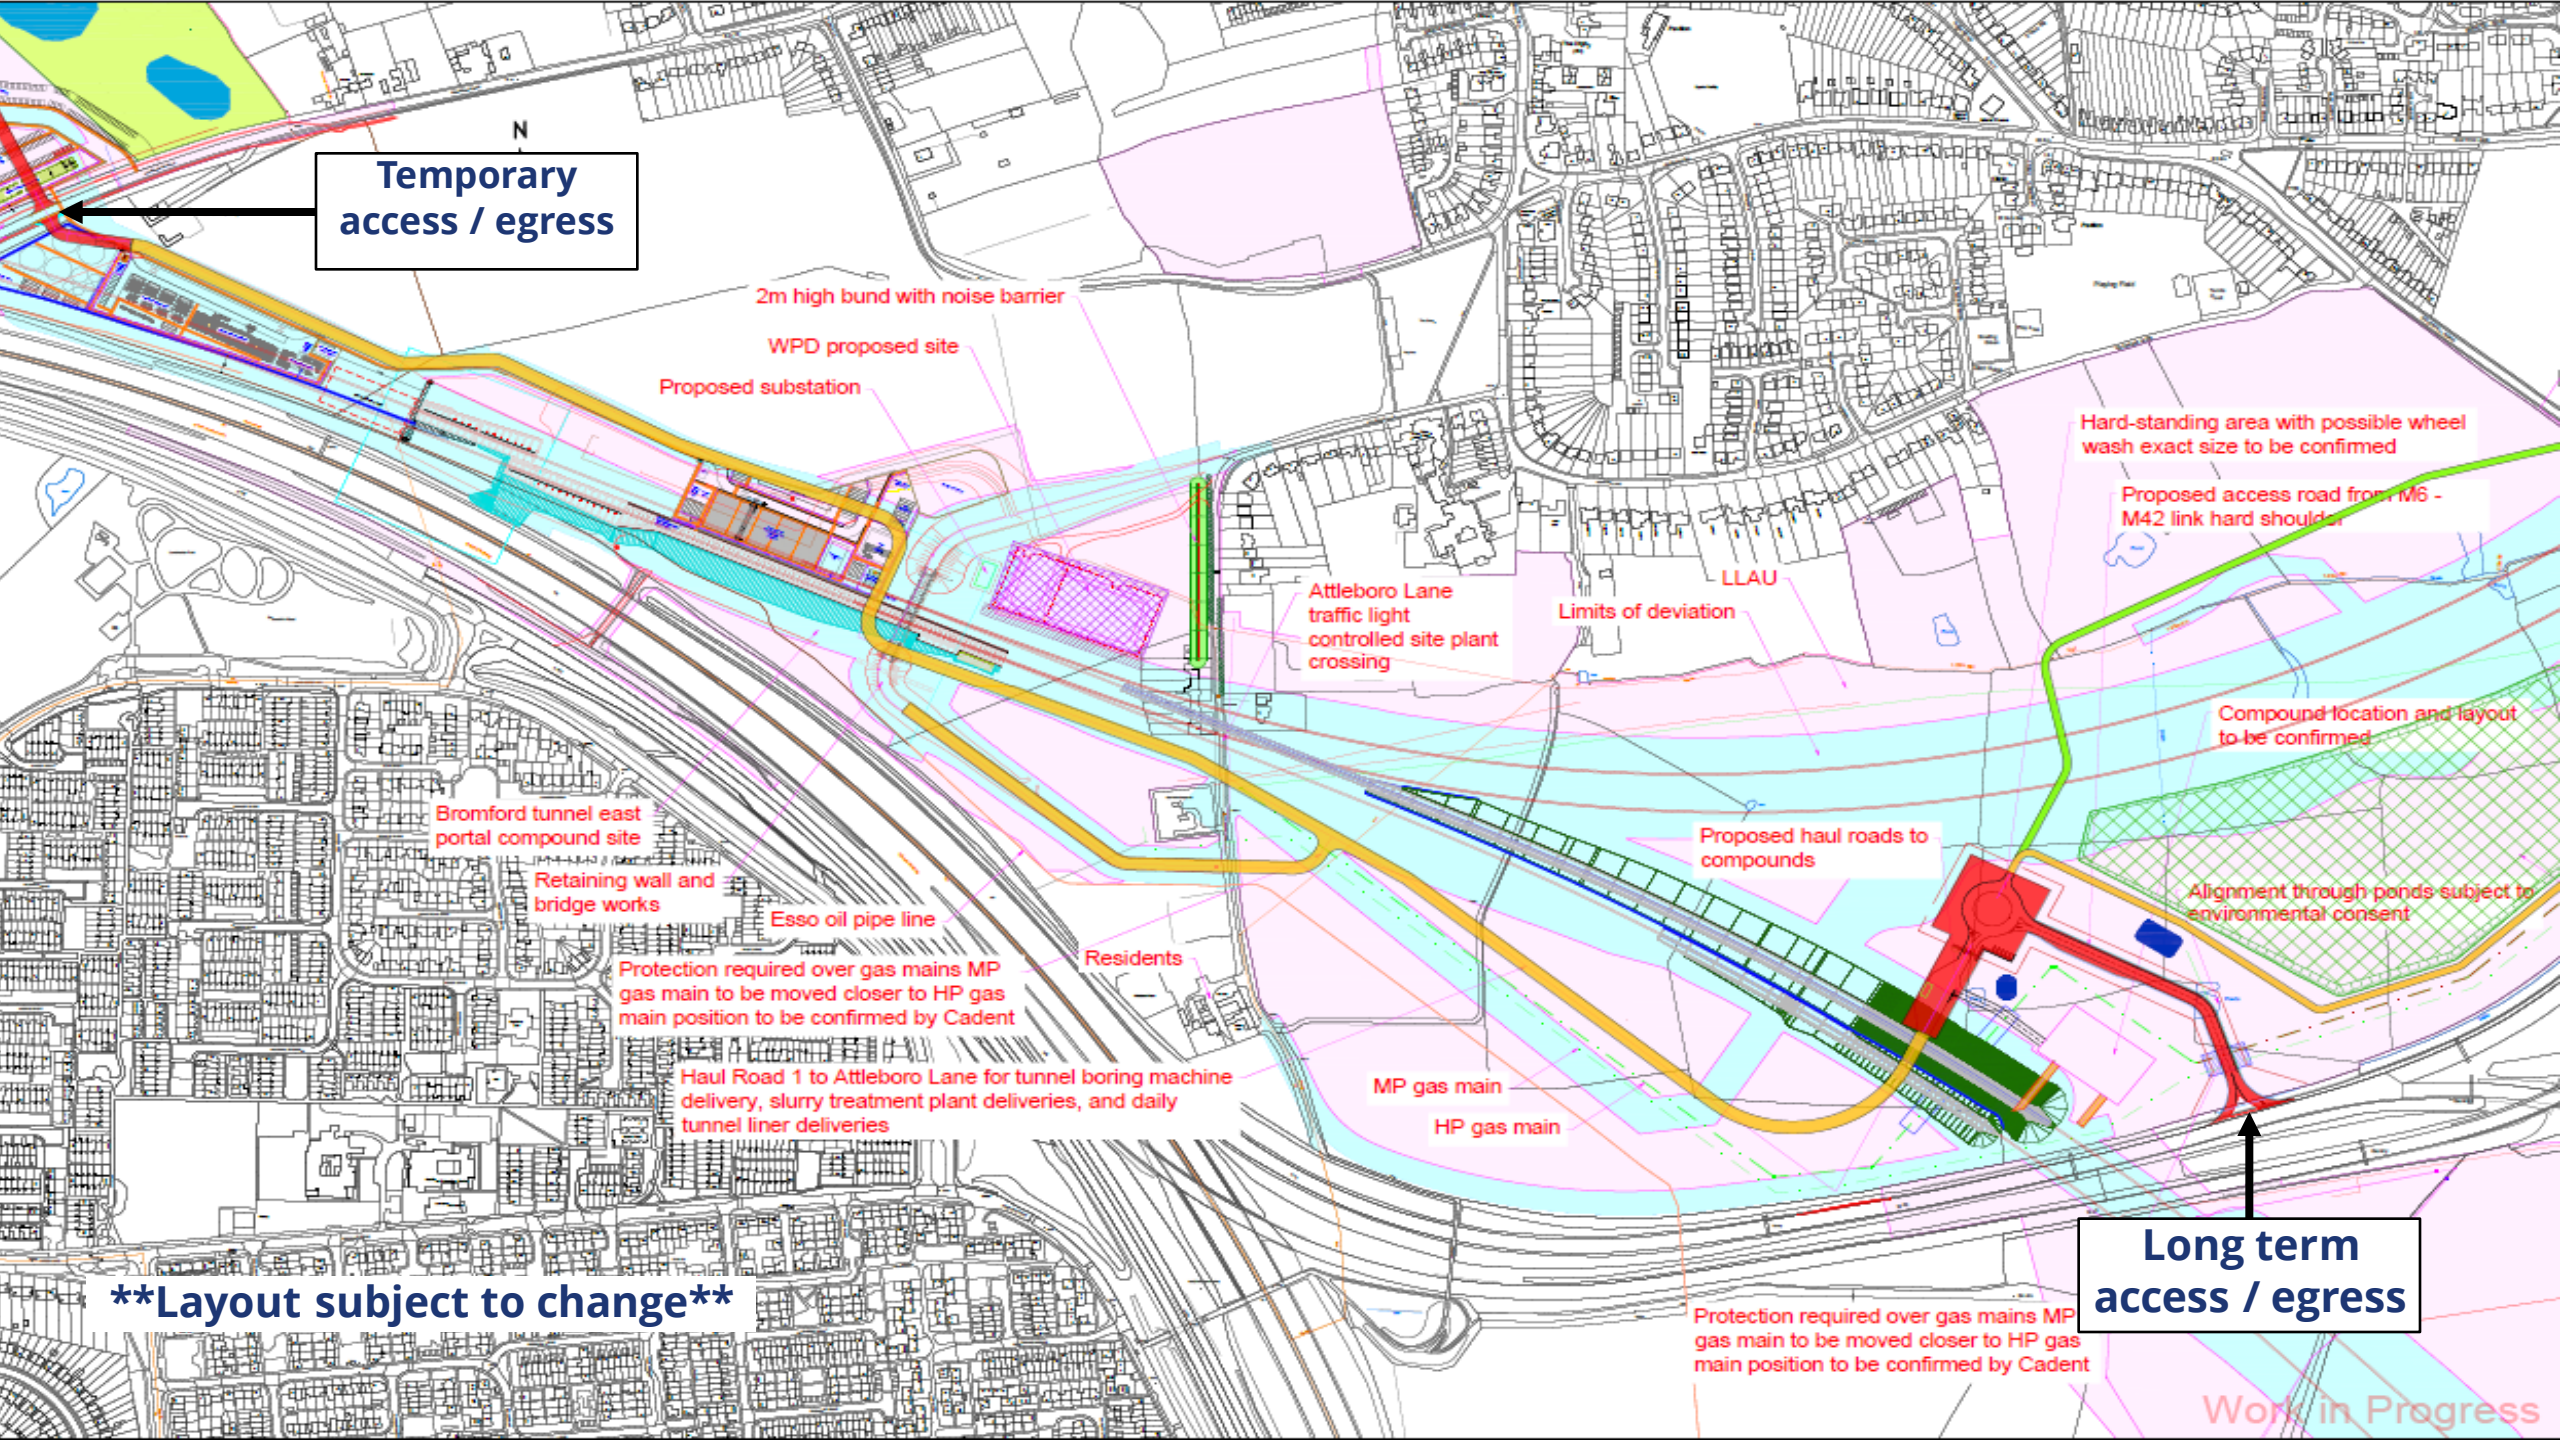
N
Temporary access / egress
2m high bund with noise barrier
WPD proposed site
Proposed substation
Hard-standing area with possible wheel wash exact size to be confirmed
Proposed access road from M6 - M42 link hard shoulder
Attleboro Lane traffic light controlled site plant crossing
Limits of deviation
LLAU
Compound location and layout to be confirmed
Bromford tunnel east portal compound site
Retaining wall and bridge works
Esso oil pipe line
Proposed haul roads to compounds
Alignment through ponds subject to environmental consent
Residents
Protection required over gas mains MP gas main to be moved closer to HP gas main position to be confirmed by Cadent
Haul Road 1 to Attleboro Lane for tunnel boring machine delivery, slurry treatment plant deliveries, and daily tunnel liner deliveries
MP gas main
HP gas main
Layout subject to change
Long term access / egress
Protection required over gas mains MP gas main to be moved closer to HP gas main position to be confirmed by Cadent
Work in Progress

Bromford East Portal

- On-going works within the compound area
- Mainly excavation works
- End of January
- Access road surfacing
- Mobilisation onto site for SB3
- Creation of platforms for compound aspects



3 month construction lookahead

- Excavation works
- Access road surfacing
- Platform creation
- Diaphragm wall creation
- Creation of compound assets

